


LEGEND




Fence/Fenced area



Vehicle path through existing tree drip line

NOTES

- Fence shall be a temporary steel fence with panels approximately 2.1 m (H) x 2.6 (W), with mesh infill. Provide weighting blocks at all junctions, minimum 35 kg each. The fence shall provide a full enclosure to the areas shown on plan and shall be sufficiently robust to serve its function to exclude vehicle and pedestrian access to the enclosed areas.
- No access or storage shall occur within the enclosures.
- Set out the fence alignments and obtain the approval of the University Arborist prior to installation.
- Outside the fenced enclosures provide measures such as diversion banks, silt traps and the like to ensure that surface stormwater patterns into the fenced areas do not differ from the conditions that prevail prior to works starting. Prevent run-off other than clean stormwater from entering the fenced enclosures.
- Provide access to the site for the University Arborist to make inspections at any time.
- Maintain the fences in a sound and effective condition throughout the construction period.
- Where access within fenced areas is necessary to implement parts of the works, give sufficient notice of the need to access and obtain the approval of the University Arborist prior to proceeding. Alter/ extend the fence as necessary to allow the works to proceed. Storage and vehicular access shall continue to remain beyond the larger fenced area.
- Do not trench within fenced areas.
- To areas allocated to construction vehicle circulation which occur within the drip line of existing trees, place approved geofabric over the area, plus for 10 m beyond in both directions, with a further 200 mm depth of virgin material 40 mm basalt ballast. Do not alter existing ground levels. Upon de-commissioning of the construction access, remove the ballast and geofabric using a small, tracked machine and cover the area with 100 mm approved Eucalypt-derived mulch.

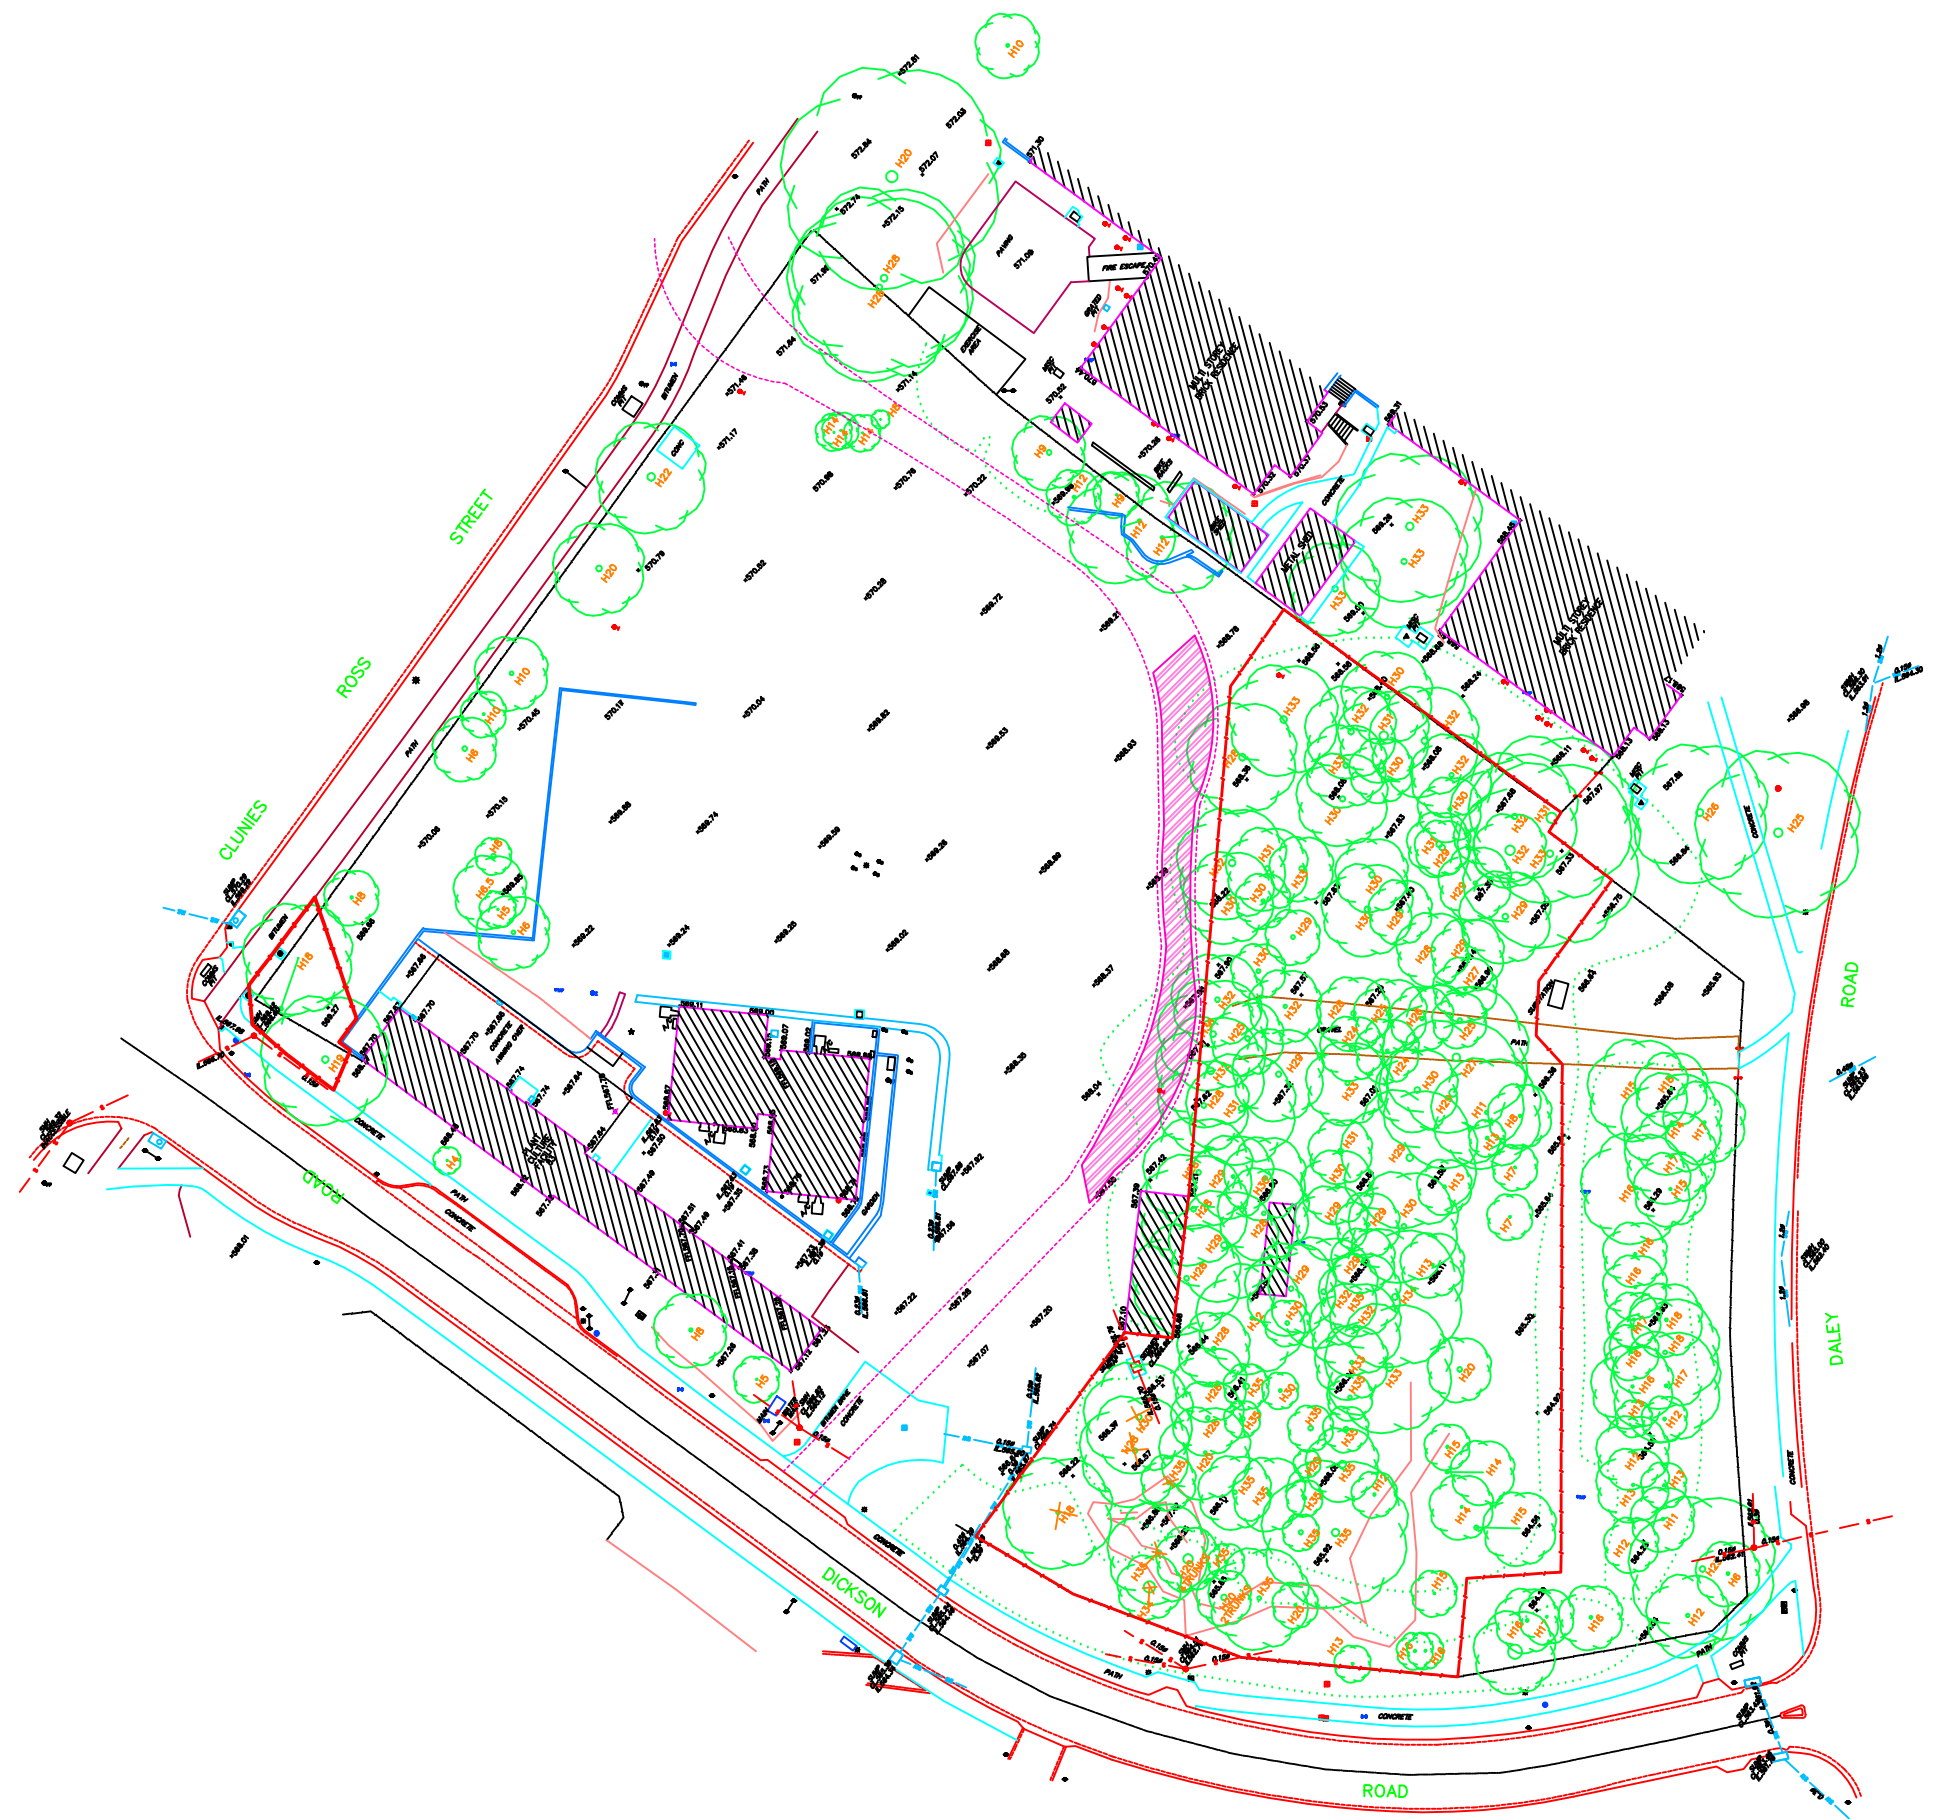

No.	Revision	Revised on CAD	do not amend by hand	Checked	Approved	Date	M/Film	STATUS
								ISSUE FOR COMMENT



Copyright
 "This document is to remain the property of Complete Urban Pty. Ltd.
 The document may only be used for the purposes for which it was commissioned & in accordance with the terms of engagement for the commission. Unauthorised use of this document in any way is prohibited"



10 Regent Street
 Chippendale NSW 2008
 p 02 9282 9900
 f 02 9282 9277




COMPLETE
 ABN 64 100 037 812
 www.completeurban.com.au

1:800
 Drawn PK
 Design PK
 Drafting Check
 Design Check
 Approved
 NOT FOR CONSTRUCTION
 This Drawing must not be used for Construction unless signed as Approved

Client and Job
 AUSTRALIA NATIONAL UNIVERSITY
 NEW HALL OF RESIDENCE
 Title
 TREE MANAGEMENT PLAN
 Drg. No. 2407-003
 Scale A3
 Rev A

DO NOT SCALE

LEGEND

-  Trees to be removed
-  Single specimen trees to be retained
-  Major group of trees to be retained



NOTE:
For protection measures for trees to be retained, refer Tree Management Plan.

No.	Revision – Revise on CAD do not amend by hand	Checked	Approved	Date	M/Film	STATUS
						ISSUE FOR COMMENT

Copyright
This document is & shall remain the property of Complete Urban Pty. Ltd.
The document may only be used for the purpose for which it was commissioned & in accordance with the terms of engagement for the commission. Unauthorised use of this document in any way is prohibited

10 Regent Street
Chippendale NSW 2008 | p 02 9282 9900 | f 02 9282 9277

COMPLETE

ABN 64 100 037 812
www.completeurban.com.au

1:800

Drawn	SE	Designed	PK
Drafting Check		Design Check	
Approved	NOT FOR CONSTRUCTION		

Client and Job
AUSTRALIA NATIONAL UNIVERSITY
NEW HALL OF RESIDENCE

Title
TREE REMOVAL PLAN

Drg. No. 2407-004

Size
A3

Rev
A

This Drawing must not be used for Construction unless signed as Approved
